




2021 Street Improvement Projects (Contract 21-101) Construction Updates August 23, 2021

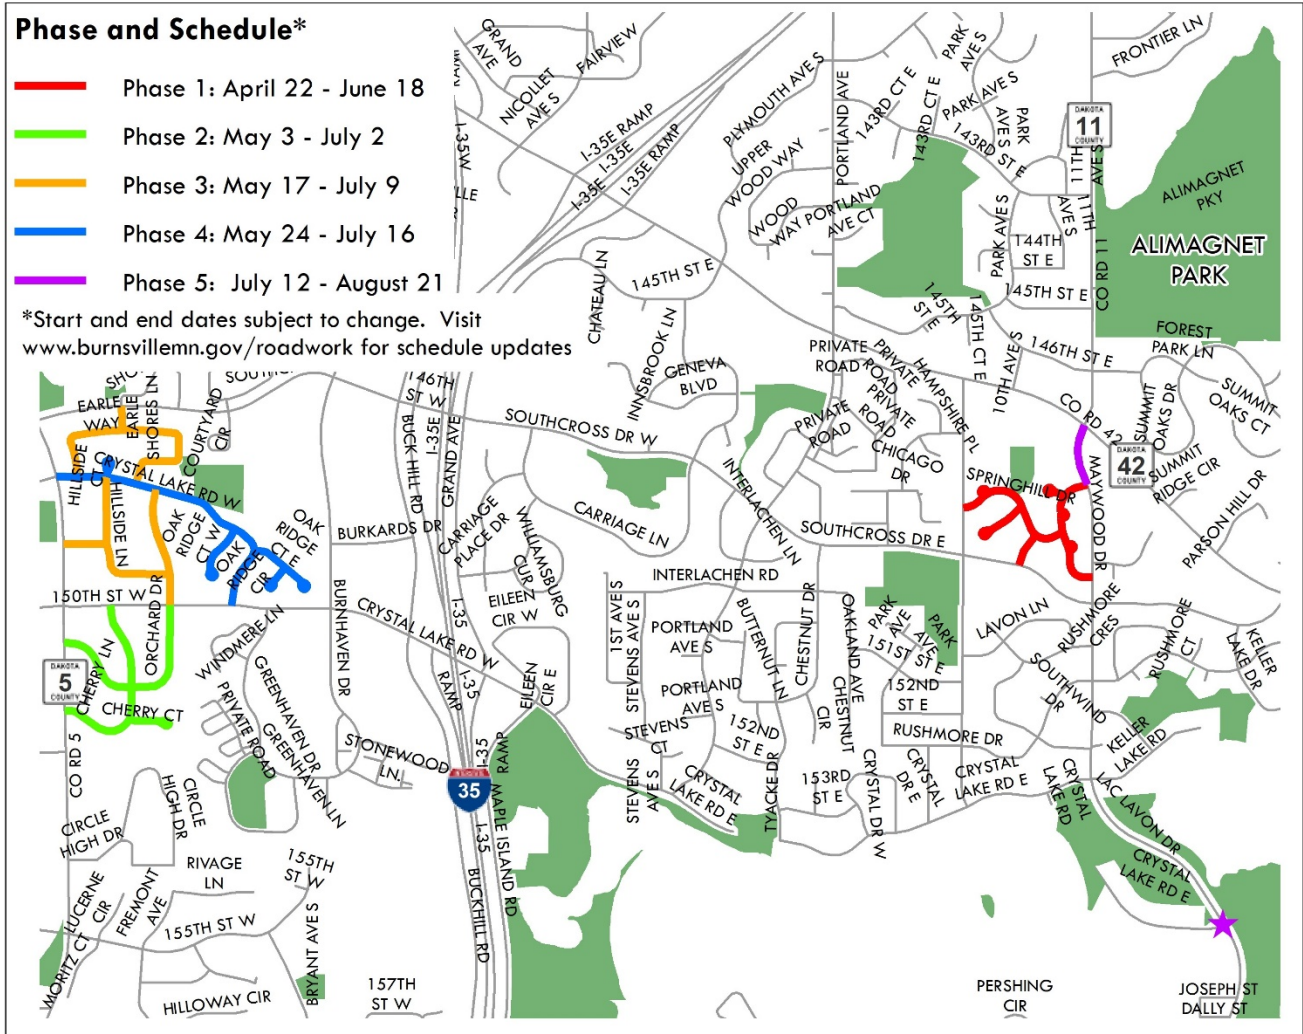

All Phases are substantially complete!

- New signs are being installed in all areas
- Re-seeding in all areas will occur after Labor Day
- Please contact the project inspector if you have any questions or concerns

Phase 1 is complete!







Phase 2 is complete!

Phase 3 is complete!

Phase 4 is complete!

Phase 5 is complete!

2021 Street Improvement Projects (Contract 21-101) Estimated Schedule by Phase*

	 Start	 Utilities	 Curb	 Grading/Paving	 Restoration	 Complete
Phase 1	Apr 22	Apr 26 – May 13	May 10-15	April 28 – May 22	May 24-29	Jun 18
Phase 2	May 3	May 3-8	May 10-15	May 10-22	May 24-29	Jul 2
Phase 3	May 17	May 17-28	May 31 – Jun 12	Jun 7-19	Jun 23-26	Jul 9
Phase 4	May 24	May 24 – Jun 5	May 31 – Jun 12	Jun 7-30	Jul 5-16	Jul 16
Phase 5	Jul 12	Jul 12-17	Jul 16-24	Jul 26-30	Jun 21-26	Aug 21

*Projected dates are subject to change based on weather and contractor operations.

Contact City Inspector Cody Pietz at 952-356-6839 or cody.pietz@burnsvillemn.gov for more information

Subscribe to email and text message updates!

Visit www.burnsvillemn.gov/roadwork and click the “Subscribe” button to sign up for email and/or text message updates.



Subscribe
